

SC Highway 160 West (Zoar Road to NC state line)

Project No. 11149-001

Project Description

The project is part of York County's Pennies-3 Program and proposes to widen approximately 1.1 miles of SC Highway 160 (from Zoar Road to the North Carolina state line) from the existing 2-lane facility to a 5-lane facility. This will add a travel lane in each direction as well as a continuous center turn lane geared towards reducing left turn movements on the mainline. The final roadway will include four-twelve-foot travel lanes, two-foot paved shoulders and a fifteen foot wide center turn lane. A traffic signal is proposed for the Zoar Road Intersection.

Status and Planned Schedule (Subject to Change)


| 2013 | 2014 | 2015 | 2016 | 2017 | 2018 | 2019 | 2020 |
|--------|------|--------------|------|--------------|------|------|------|
| Design | | Right of Way | BID | Construction | OPEN | | |

Condition At-a-Glance

| Attribute | Current Status | Action Plan |
|-----------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------|
| Scope | Y Right-of-Way Design/Environmental Documents in progress. | Submit Right-of-Way Plans to SCDOT for review. |
| Schedule | Y Design is underway. | Ongoing |
| Costs | R Preliminary construction quantities will not be submitted for the development of the estimate until Right-of-Way Plans. Current estimate based on original budget. | Project costs will be compared once bids are received |
| Overall | R Project is still in the early stages of design and may experience changes as the design continues | Award contract once bids are let and received, sign contracts, construct project (estimated 15 months) |

Attribute Symbol Legend: G Not likely to change. Y Change possible. R Likely to change.

Map

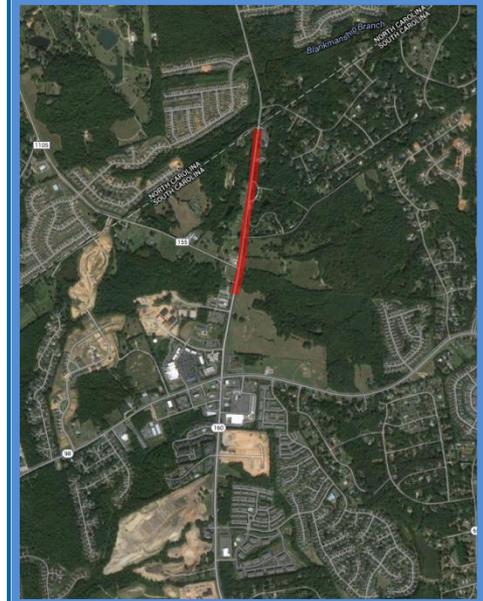

Project Funding

| Phase of Work | Amount (\$) |
|-------------------------|------------------|
| Preliminary Engineering | 1,150,335 |
| Right-of-Way | 1,327,309 |
| Construction | 6,371,084 |
| Total | 8,848,728 |

Project Budget

| Source | Amount (\$) |
|-----------------------------------|------------------|
| Local (Pennies for Progress) 100% | 8,848,728 |
| Total | 8,848,728 |

Project Updates (August 31, 2015)

Evaluate driveway access. Prepared preliminary utility report. Conducted Right-of-Way Design Field Review with SCDOT and York County.
